



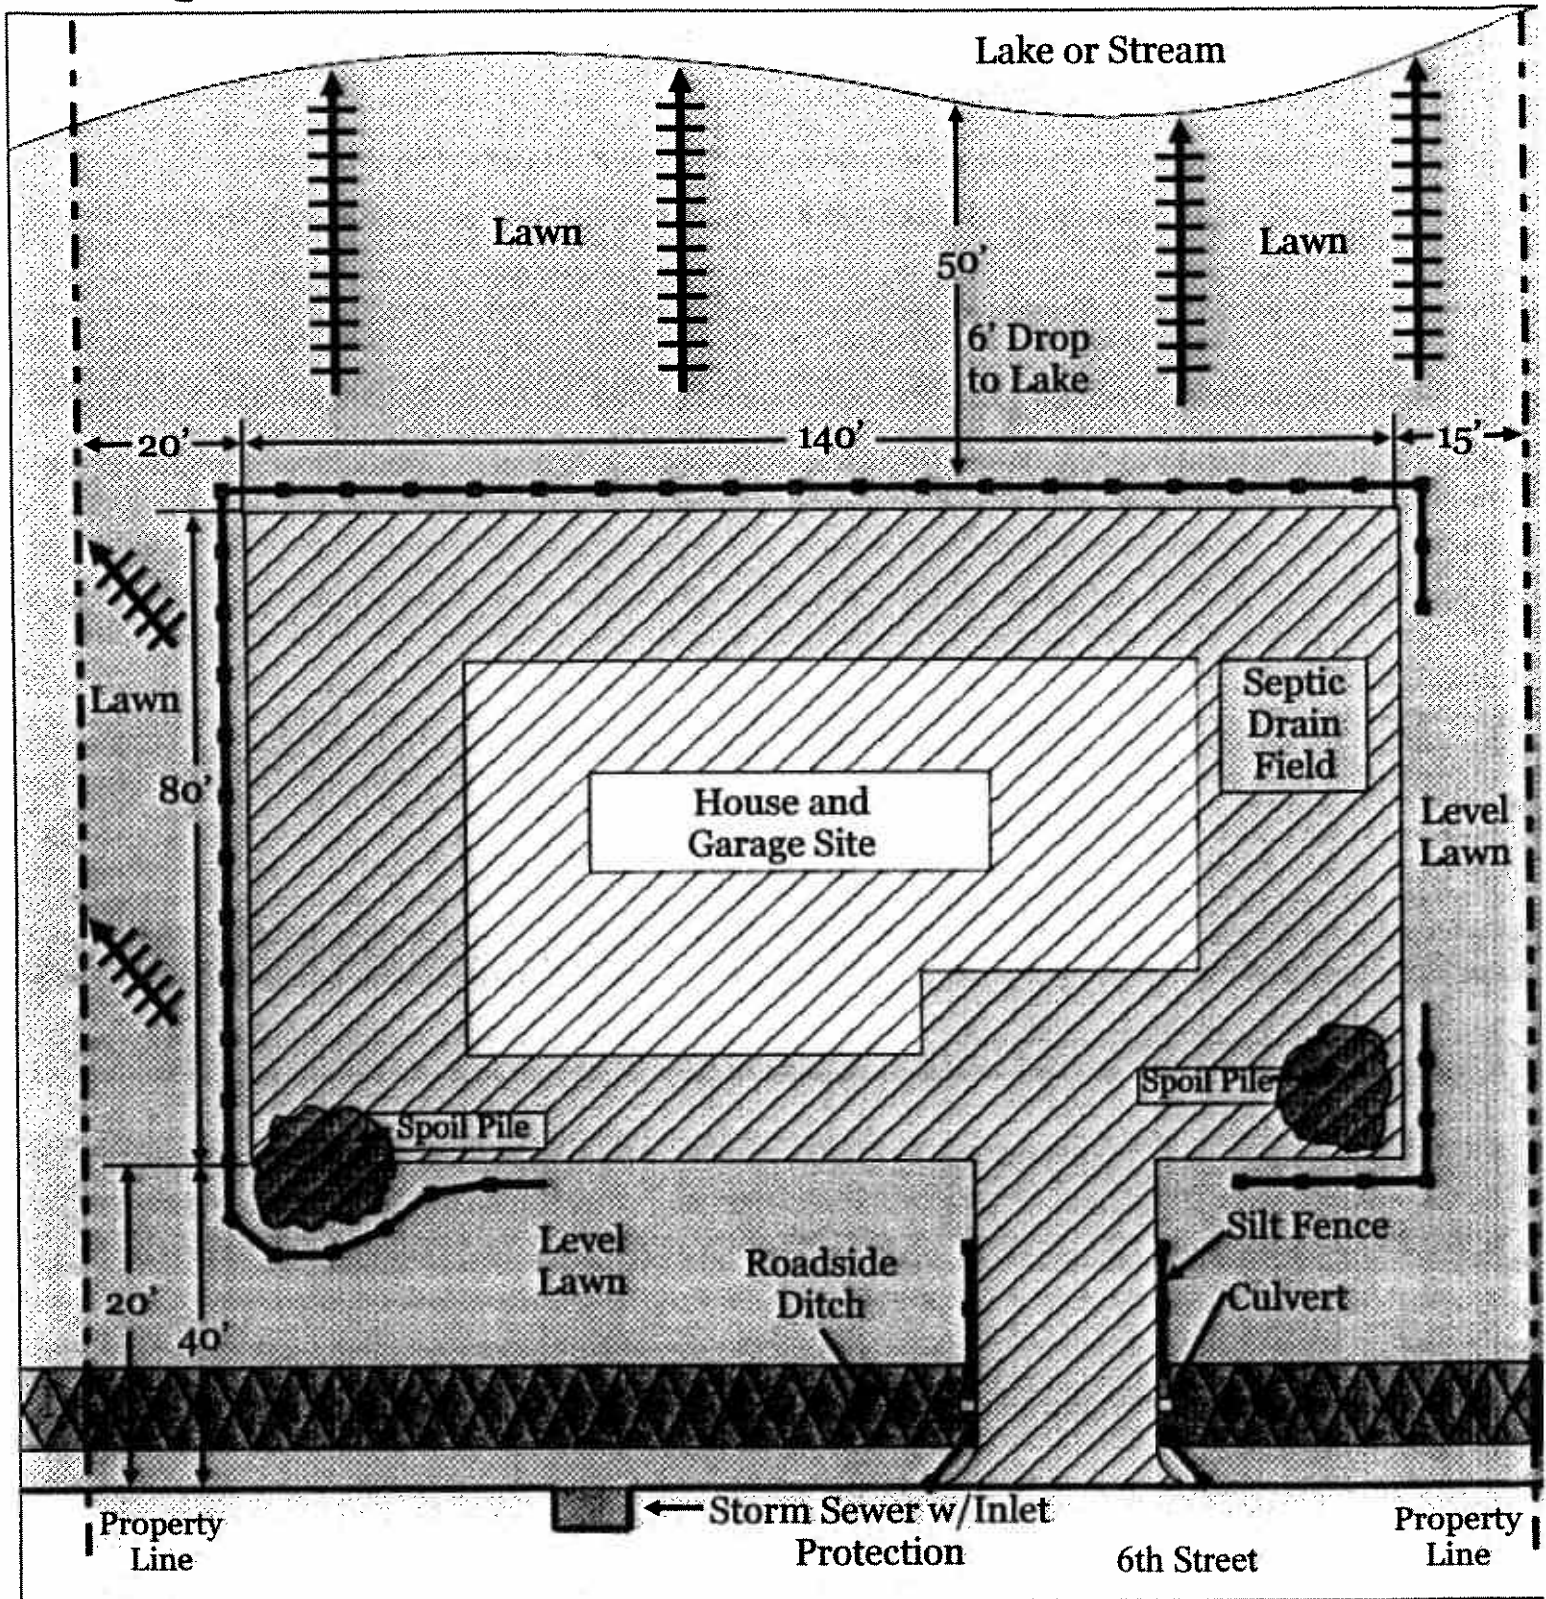


# Sample Site Plan: Soil Erosion and Sediment Control Plan



## Legend

-  Area of Disturbance
-  Direction of Slope
-  Silt Fence

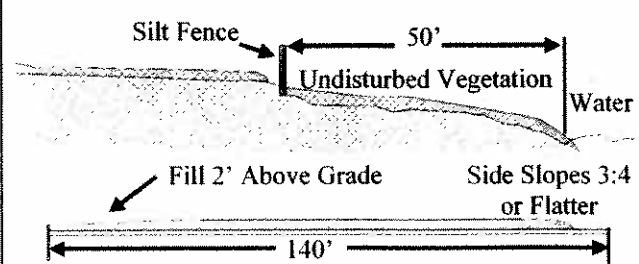

## Schedule

- 6/15 - Install perimeter sediment controls
- 6/17 - Grade site
- 6/17 to 9/10 - Construction of home
- 9/15 - Pave driveway
- 9/15 to 9/20 - Final grade, seed and mulch, perimeter controls will be removed when grass is established.
